



Bond 2020 Community Update

Collins Garden Elementary Graebner Elementary Burbank High School

Jan. 30, 2025

www.saisd.ne

Purpose of Today's Meeting

- Bond 2020 Program Update
- Major renovation updates for:
 - Collins Garden Elementary
 - Graebner Elementary
 - Burbank High School
- Facility Condition Assessment and master planning





Bond 2020 Approval

In November 2020, voters approved two propositions totaling \$1.3 billion:

PROP A

\$1.21 billion for:


- Campus renovations/upgrades, including HVAC upgrades
- Security upgrades at all schools
- Replacement of air-conditioning chillers more than 15 years old at schools not receiving major renovations
- New school models

PROP B

\$90 million for technology upgrades for all schools



Bond 2020 Planning

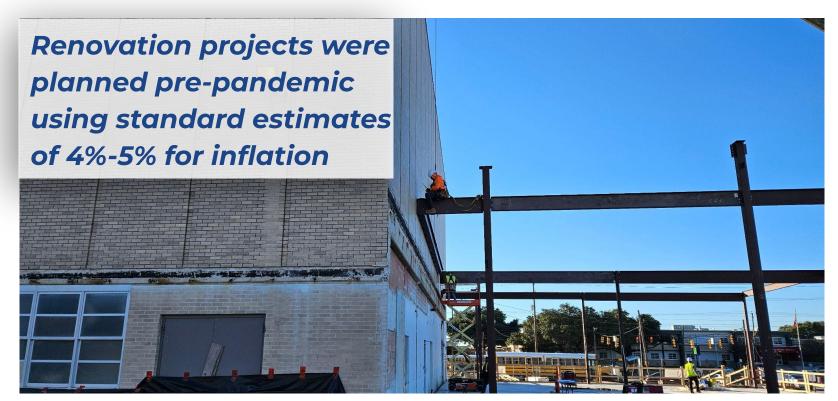




Pandemic Impacts

And then the global pandemic hit, bringing with it significant construction pressures:

- Unprecedented inflation
 - Average of 25-30%
 - Preliminary estimates for all projects came in over budget
- Supply chain issues
- Labor shortages

Estimated vs. Actual Average Inflation





District Response


A tremendous amount of work went into salvaging Bond 2020:

- Bond expenses examined at a program and a project level to identify savings
- A number of program-wide cost-saving measures implemented
 - Example: project start dates staggered through phasing
- Every major renovation project reviewed to get as close to budget as possible





How Can Bond Funds Be Used?

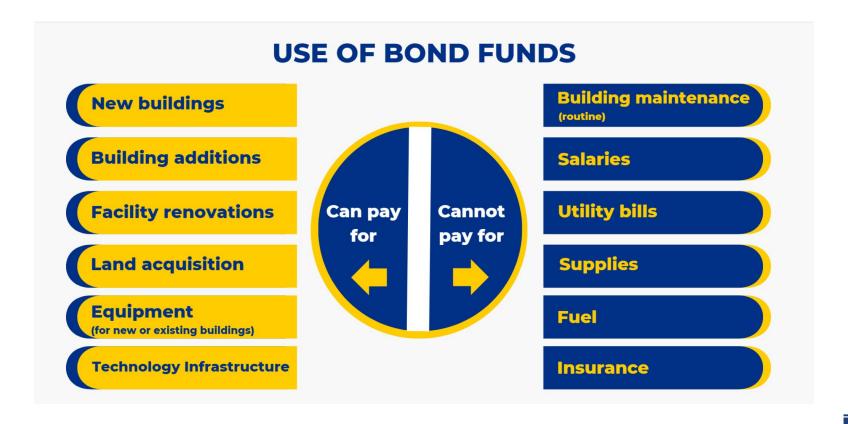



Rightsizing Impact

In 2023, the Board of Trustees voted on a plan to consolidate SAISD schools

- Ripple effect on the bond program
- 7 of the campuses to be consolidated were slated for renovations (leaving 29 major renovations projects)
- Receiving campuses had immediate needs to accommodate larger student populations





Funds From Canceled Bond Projects


Funds returned to the overall bond program for areas of critical need across the district, including at campuses receiving students through Rightsizing

- The Bond 2020 Citizens Advisory
 Committee supported the use of returned bond funds for the following priority areas:
 - ☐ HVAC
 - Security upgrades
 - ☐ Restoration of scope to address critical needs





Significant HVAC Needs

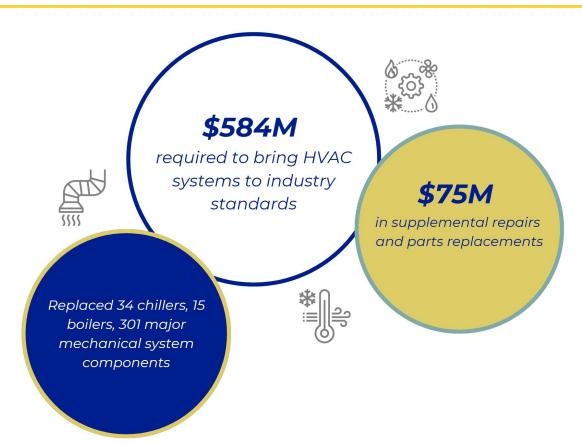



Where We Are Today





Breakdown of Project Costs





Graebner ES: Current Project Scope & Budget

Total Budget*: \$45.6 million

Scope:

- New 2-story academic building with classrooms, science labs and support spaces
- New Library
- Music rooms for Mariachi and Orchestra
- Renovate kitchen and cafeteria.
- New playground
- Renovate existing parking lot
- Landscaping throughout the site

*Includes architectural, engineering, surveys, permits, construction costs and FF&E

Phase 3 Project

Targeted completion: Summer 2026



Graebner ES Project Status

Overall project: 34% complete

New academic building: 20 classrooms; to be completed summer 2025

Renovated 2001 wing: Renovation to be completed fall 2025

Up next: New boiler and chiller to be installed winter 2026





Graebner ES Project Status



Burbank HS: Current Project Scope & Budget

Total Budget*: \$24.6 million

Scope:

- Additional classrooms
- New gym
- Coaches' offices
- Laundry room
- Mat/weight room
- Storage areas
- Athletic fields, track, and tennis improvements

Phase 2 Project

In Design

*Includes architectural, engineering, surveys, permits, construction costs and FF&E



Collins Garden ES: Current Project Scope & Budget

Total Budget*: \$35.6 million

Scope:

- New administrative building
- New kitchen, dining and music space
- Renovate existing academic building (classrooms)
- Touch up historic courtyard
- HVAC, Technology, and Security upgrades

*Includes architectural, engineering, surveys, permits, construction costs and FF&E

Phase 3
Project

In Design



Phase 3 Projects

Most Phase 3 projects are in the design phase

- Construction estimates for most Phase
 3 projects exceed project budget
- As we review Phase 3 projects, key factors to consider include next round of Rightsizing and SAISD Master Plan 2045





Next Round of Rightsizing

In May 2024, the Board of Trustees requested recommendations for next round of Rightsizing

- SAISD still has more schools than it needs for current student population of about 44,000
- Kicking off Master Plan 2045 to guide future downsizing efforts





About the Master Plan

Master Plan 2045
will provide
significant data
for each SAISD
facility



INDEX

Numerical value that measures the condition of a facility by comparing the cost of repairs to the cost of

replacing the facility








Next Steps

 Kick off the facility master planning process to chart a new way forward for facilities in SAISD



Capital Development & Construction
 Services will be following up with
 principal to discuss formation of Project
 Advisory Team (PAT).



Bond Update & News

Bond.saisd.net

For individual project updates, upcoming events, and more

Campus website

Quick link to your school's bond page via your campus homepage

Social media

Follow **SanAntonioISD** on Facebook, Instagram, and LinkedIn for bond progress and event info











Questions



